

5. PROJECT PLANNING & SCHEDULING

5. PROJECT PLANNING & SCHEDULING

Date	01 October 2026
Team ID	SWTID-2026-4302
Project Name	Import Data using Transform Maps (Spreadsheet)
Team Members	Prasanna K, Yousuf Riyas S, Ratnakar K S, Mohammed Thoufiq I

5.1 Project Planning

Work was planned using Agile Scrum. The project is split into **Epics** (large functional areas), each broken into **Stories** that fit inside a **Sprint** (a fixed work period). Each story gets **Story Points** that show effort on a Fibonacci-style scale: 1 = very easy, 2 = normal, 3 = moderate, 5 = difficult. The 15 user stories total **38 story points** across four sprints that follow the three milestones plus reporting.

Product Backlog and Sprint Planning

Sprint	Functional Requirement (Epic)	Story No.	User Story / Task	Story Points	Priority	Team Member
Sprint-1	Spreadsheet Preparation	USN-1	As an administrator, I can create a new Google Spreadsheet with sample employee data (Employee ID, Employee Name, Email, Department, Location).	1	High	Yousuf Riyas S
Sprint-1		USN-2	As an administrator, I can download the spreadsheet as Sample Spreadsheet.xlsx.	1	High	Yousuf Riyas S
Sprint-1	Table Creation	USN-3	As an administrator, I can create the custom table Employee Test (u_employee_test).	2	High	Prasanna K
Sprint-1		USN-4	As an administrator, I can add Employee ID, Employee Name, Email, Department and Location as String fields using Form Layout.	2	High	Prasanna K
Sprint-2	Import Set Table	USN-5	As an administrator, I can use Load Data to create the Employee Import (u_employee_import) staging table from the spreadsheet.	3	High	Ratnakar K S

Sprint	Functional Requirement (Epic)	Story No.	User Story / Task	Story Points	Priority	Team Member
Sprint-2	Transform Map	USN-6	As an administrator, I can create the transform map Sample Spreadsheet Import (Employee Import to Employee Test) and auto-map matching fields.	3	High	Mohammed Thoufiq I
Sprint-2		USN-7	As an administrator, I can run the transform and see a success message.	2	High	Ratnakar K S
Sprint-3	Transform & Validate	USN-8	As an administrator, I can open the Employee Test table and verify the imported records, arranging columns with Personalize List Columns.	1	High	Yousuf Riyas S
Sprint-3		USN-9	As an administrator, I can validate that required fields (Employee ID, Name, Email) hold valid data so incorrect or incomplete rows can be corrected.	2	Medium	Mohammed Thoufiq I
Sprint-3	Coalesce	USN-10	As an administrator, I can set Coalesce to true on the Employee ID field map.	3	High	Prasanna K
Sprint-3		USN-11	As an administrator, I can import an updated sheet (4 rows: 2 existing IDs with changed name/email and 2 new IDs) and have existing records updated and new ones inserted.	5	High	Ratnakar K S
Sprint-3		USN-12	As an administrator, I can re-import the same sheet without creating duplicates.	2	High	Mohammed Thoufiq I
Sprint-4	Reports	USN-13	As an HR user, I can view reports on Employee Test: Employees by Department (pie chart), Employees by Location and Employee List.	5	Medium	Yousuf Riyas S
Sprint-4	Dashboard	USN-14	As an administrator, I can create the Employee Analytics Dashboards (enabling Admin Overrides on the pa_dashboards create ACL when the form is opened by its backend name).	3	Medium	Prasanna K
Sprint-4		USN-15	As an administrator, I can add the three reports to the dashboard and restrict sharing by users, groups and roles.	3	Medium	Mohammed Thoufiq I

Sprint Schedule and Project Tracker

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed (on planned end date)	Sprint Release Date (Actual)
Sprint-1 (Milestone 1)	6	6 Days	05 Oct 2026	10 Oct 2026		
Sprint-2 (Milestone 2)	8	6 Days	12 Oct 2026	17 Oct 2026		
Sprint-3 (Milestone 3)	13	6 Days	19 Oct 2026	24 Oct 2026		
Sprint-4 (Reports & Dashboard)	11	6 Days	26 Oct 2026	31 Oct 2026		

Dates are proposed planning dates (Monday to Saturday). The last two columns are filled by the team as each sprint finishes.

Team Workload

Team Member	Assigned stories	Story points	Share of total
Prasanna K	USN-3, USN-4, USN-10, USN-14	10	26%
Yousuf Riyas S	USN-1, USN-2, USN-8, USN-13	8	21%
Ratnakar K S	USN-5, USN-7, USN-11	10	26%
Mohammed Thoufiq I	USN-6, USN-9, USN-12, USN-15	10	26%
Total	15 stories	38	100%

Velocity

Velocity = total story points completed ÷ number of sprints.

Sprint	Story Points
Sprint-1	6
Sprint-2	8
Sprint-3	13
Sprint-4	11
Total	$6 + 8 + 13 + 11 = 38$

Velocity = $38 / 4 = 9.5$ story points per sprint. Average velocity per day (6-day sprint) = $9.5 / 6 = 1.58$ story points per day.

Burndown Chart

A burndown chart shows work left to do versus time. The chart below is the planned burndown across the four sprints (38 → 32 → 24 → 11 → 0 story points); the team adds the actual remaining points after each sprint.

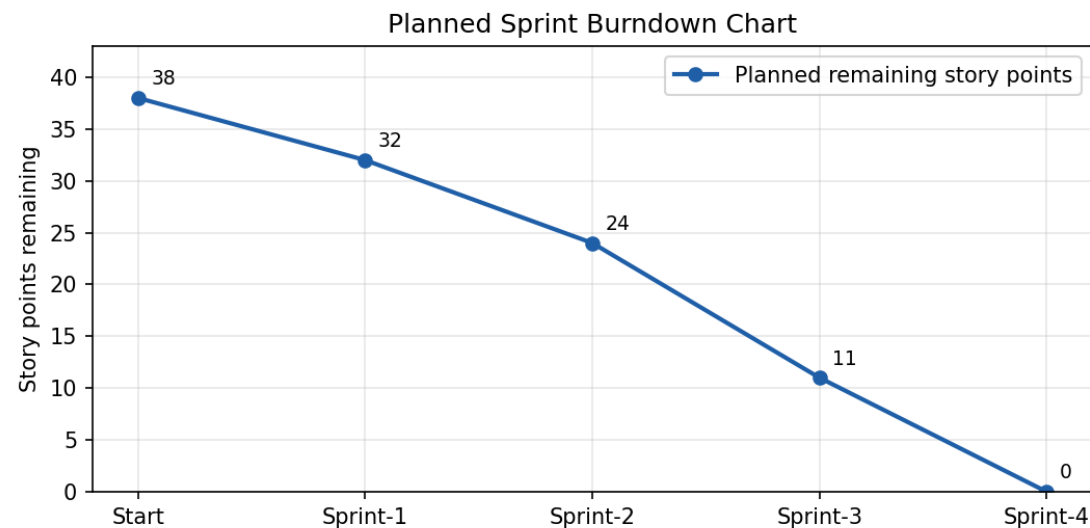


Figure 5.1 – Planned burndown across the four sprints

Reference: <https://www.atlassian.com/agile/tutorials/burndown-charts> | <https://www.atlassian.com/agile/project-management/estimation>
